

Network Engineering Technologies -3140 Deming Way Middleton, WI 53562 P: 608.827.6700 F: 608.827.6705 www.nettechnology.com

Your VendorID:	60426
Purchase Order:	614377-1253026-02943
Work Order:	1253026
Service FTA	9/14/20 at 11:00 AM

* Purchase Order MUST appear on all invoices and emailed to apinbox@nettechnology.com or invoice will be rejected, Invoice must match this Purchase Order Receipt.

TECHNICIAN INFORMATION
Technician Name: Marlon Dardaine Technician Phone: (347) 793-4164
Techs Manager: LaToya Cutliff
Manager Phone: 40580212620000

*** MUST CALL UPON ARRIVAL AND BEFORE SITE DEPARTURE

NET Contact Please Call: 1 608 827-2283 *Your call will be handled in the order received*

Info: The following Login information is needed: your name, Company Name, work order#, callback number(mobile#)

Schedulina

1 billable technician required Arrival Time: 9/14/2020 11:00:00 AM

Scope of Work

CVS - Demarc to Phone Cabinet [Troubleshoot] / [Extend] Elevator Line

NET techs will LOG IN/LOG OUT LIVE by calling (608) 827-2283. DO NOT AUTO LOG IN*

Elevator Phone Line will either be set up as Scope 1 or Scope 2 below.

[SCOPE 1] Need tech to troubleshoot/extend connection for elevator line [404-892-8473] from the demark to the A-row (Green Jacks) located in the white phone cabinet. All store lines should come in on the orange telco 66 block and then cross connect over to (2) subsequent CVS 66 blocks. One of the 2 CVS blocks will have a 25 pair Amphenol cable that runs to the A row in the white phone cabinet which is typically located in the Manager's office or in the back demark area. Once dialtone is restored to the A row tech will need to cross connect to cable run that runs out to the elevator control room on the 100/200 series jack. Tech will need to press the call button in the elevator to test outbound call.

[SCOPE 2] Need tech to troubleshoot/extend connection for new elevator line [404-892-8473] from the demark to the elevator control room. Tech will need to find dialtone on the orange telco 66 block and then cross connect cable run that goes out to the elevator control room. Once cross connect is made at the demark, dial tone needs to be confirmed at the other end of the jack in the elevator control room. Jack should be labeled with the phone number. Tech will need to press the call button in the elevator to test outbound call.

Currently, there is cross talk on the line going to the elevator that is out of code.

Phone - TECH WILL NEED BUTTSET for testing purposes


IF TECH IS UNABLE TO RESOLVE CABLING ISSUE WITHIN 1 HR. TECH WILL PULL A NEW CABLE. TECH SHOULD ASSUME A NEW CABLE WILL NEED TO BE PULLED AND HAVE THE NECESSARY MATERIALS TO COMPLETE THE PULL ON THIS SERVICE CALL.* FAILURE TO COMPLY WITH ANY PORTION OF THIS WORK ORDER MAY RESULT IN NON-PAYMENT.*

Required Photos

1) Demarc Overview

2) Close up of Phone Can (if applicable)

Continued from Page 1 of 2

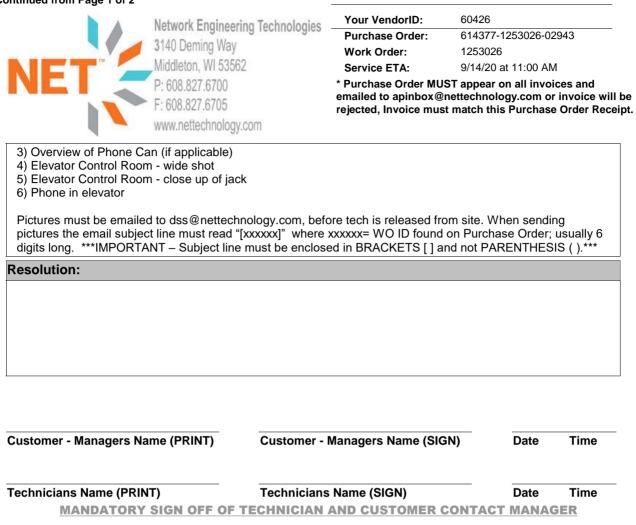

Sign Off does not release tech from the job site. Any questions need to be directed to NET Tech Support.
